

Calgary



# Green Line Committee

## Green Line LRT Project Update

March 31, 2021

CITY OF CALGARY  
RECEIVED  
IN COUNCIL CHAMBER

MAR 31 2021

ITEM 7.1 GC 2021-0488  
DISTRIBUTION  
CITY CLERK'S DEPARTMENT

# Agenda

- I. Green Line Board
- II. Green Line Project Update
- III. Provincial Review
- IV. Segment 2 Functional Planning Update






# Green Line Board





## Green Line Board

Don Fairbairn

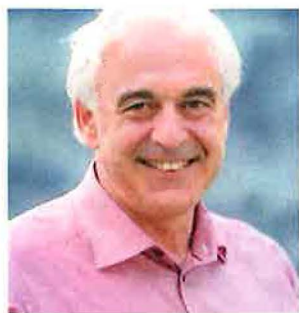

Larry Beasley



Ian Bourne



Marcia Nelson



Janet Annesley



Fred Cummings



David Duckworth



Bharat Mahajan




Patricia McLeod



# Green Line Board Reporting Structure

## Flow of Reporting on Green Line through Committees to Council

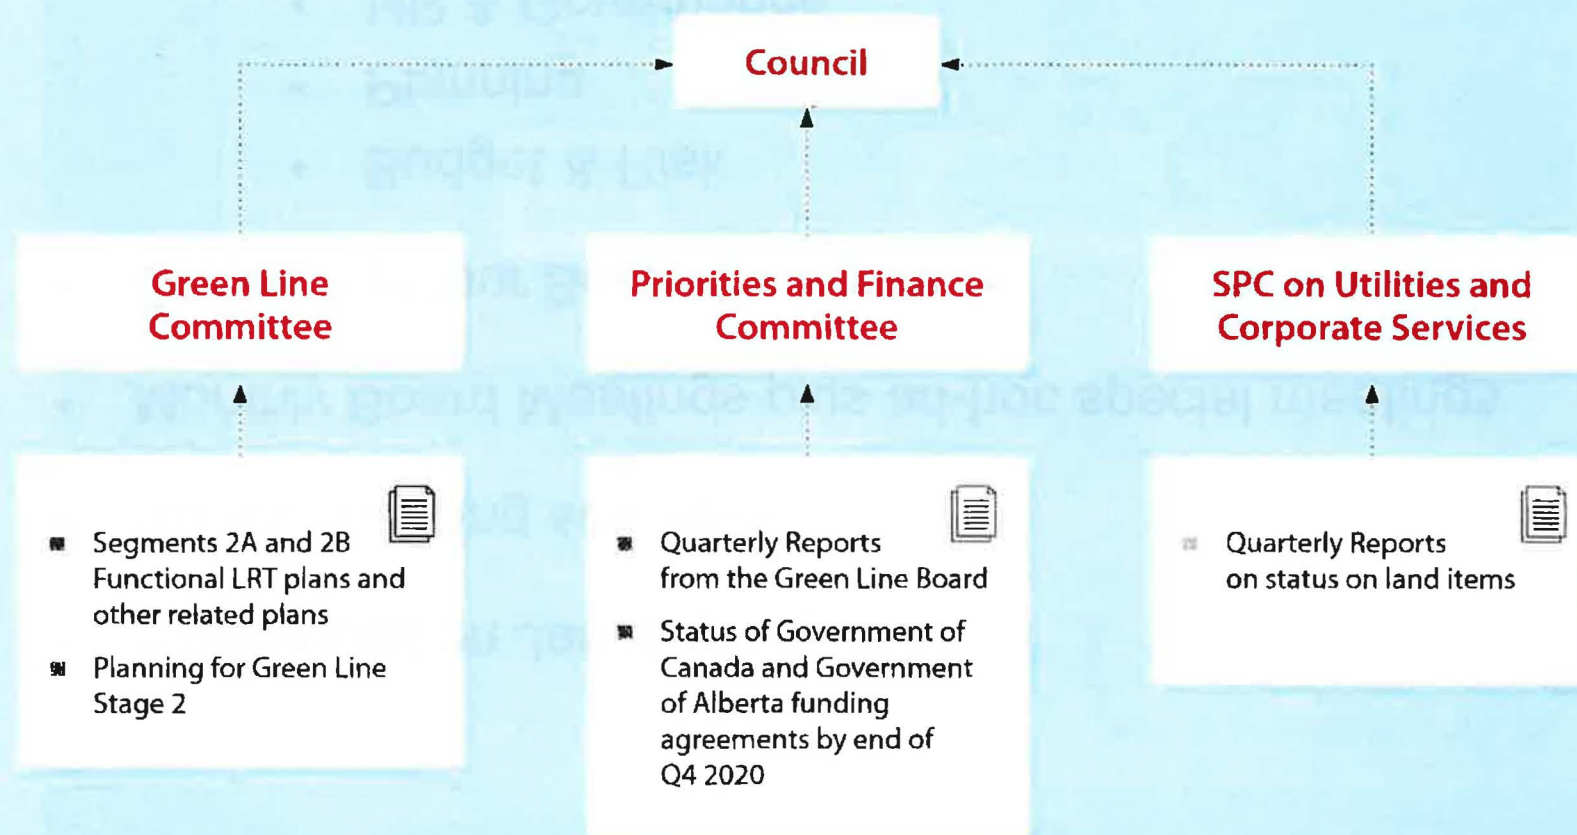

July 13, 2020 - Green Line Governance  
GLC-2020-0772



# Green Line Board Update

- Announced on January 14, 2021
- Six on-boarding sessions
- Monthly Board Meetings plus ad-hoc special meetings
- Creation of four Board Committees
  - Budget & Risk
  - Planning
  - HR & Governance
  - Recruitment Committee

# Green Line Project Update



## Q1 2021 Updates

- Segment 1 Enabling Works
  - CN Highfield work is 90% complete
  - Ongoing work with CP (78<sup>th</sup> Avenue, Ramsay/Inglewood)
- Launched Business Insights Panel
- Real Estate
  - Advancing Segment 2 Station Integration discussions
- Current Procurements
  - LRV
  - Construction Manager (CM)
  - Segment 1 LRT Construction (paused)



## Construction Manager RFP

- CM Utility Relocation Project RFP closed on February 4, 2021
- Green Line Board accepted recommendation and negotiations are currently underway
  - Expected announcement in April 2021
- \$138M Utility Relocation program in Beltline/downtown
  - Multi-year project that will transition to main construction
  - Not funded through Enabling Works – program cost
- Construction will begin by Fall 2021 (Aug/Sept)

# Provincial Review



## Provincial Review Status

- Multiple meetings per week between City and Province
  - Letter from Minister McIver acknowledging collaboration received on March 19, 2021
- Most items identified in the Review have been addressed with the province
- Confidential market sounding held in February/March
  - 24 builder/designers, tunnel companies and lenders



## Segment 2 Functional Planning Update



## Segment 2 Functional Plan

- Following Council direction, functional planning for Elbow River to 16<sup>th</sup> Avenue is nearing completion
  - Beltline
  - Downtown/Eau Claire
  - Bow River Bridge
  - Centre Street N
- Final Inform stage begins week of April 12, 2021
  - Council
  - Key partners
  - CA/BIA
  - Community members
- Present to Green Line Committee – May 2021

## Recommendation

That Green Line Committee of Council receive Verbal Report GC2021-0488 for information and the presentation for the corporate record.



# Questions

