



Green Line Update

EC2025-0849

September 8, 2025

Previous Council Direction

- 17 September 2024 – Regular Council
- 8 October 2024 – Public Hearing Council
- 26 November 2024 – Regular Council
- 17 December 2024 – Regular Council
- 14 January 2025 – Public Hearing Council
- 28 January 2025 – Regular Council

Recommendation:

That Executive Committee recommend Council receive this report for the Corporate Record.

✓ Groundbreaking

- ✓ Shovels hit the ground on June 26, 2025.
- ✓ Participants from all three levels of government.

✓ Current Works

- ✓ Geotechnical program in progress, to support design progression.
- ✓ Construction at the MSF site began in early July, following the groundbreaking.
- ✓ 114 Ave and Barlow piling and road configuration underway.


✓ 2025 Procurement & Construction

- ✓ Three packages to be awarded in September.
 - 78 Avenue LRT Bridge, Ogden Road Realignment and Blackfoot Trail LRT Bridge
- ✓ RFPQ for 2026-2031 main civil construction in market, closing September 22, 2025.



Downtown Segment

- ✓ Consultant contract being finalized; detailed work plan under development.
- ✓ Engagement plan being developed.
 - ✓ Formal public engagement to begin Q1 2026.
 - ✓ More detailed update on communications/engagement coming to Council in December 2025.
- ✓ Utility relocation on 2 Street SW has resumed; work continues through Q1 2027 to clear corridor.
 - ✓ Enmax to begin relocation work on 6 Avenue (1 St – 3 St SW) in September 2025.

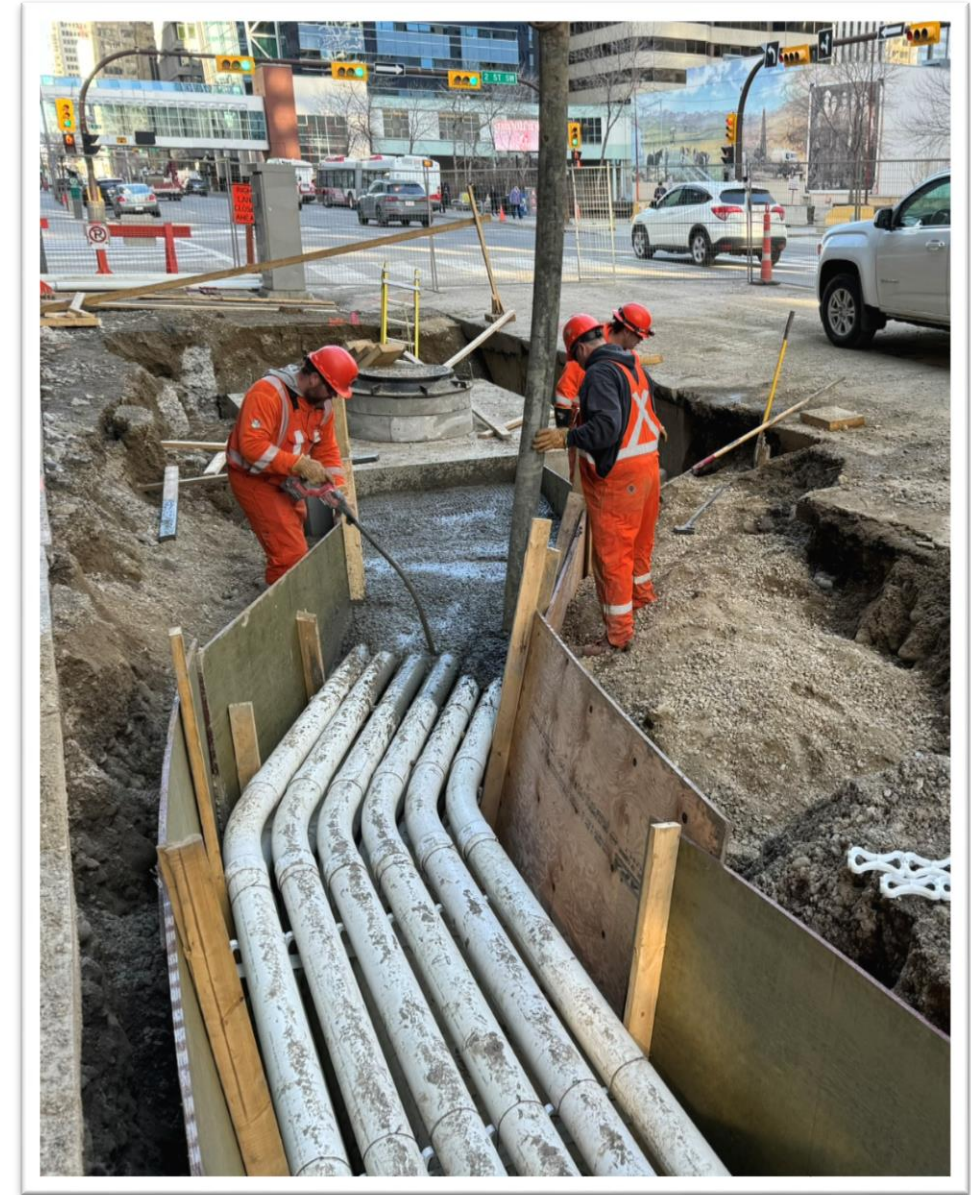

Utility Relocation Work on 6 Avenue SW



Green Line LRT Project Financial Summary

Financial Summary – (in\$) – End of July 2025

Category	Committed Cost	Cost to Date	Cost Year to Date
Owner's Cost	123,511,419	119,270,355	7,798,870
Land, LRV & Other Assets	557,875,561	388,848,739	32,372,169
Engineering, Procurement & Construction	1,078,350,457	998,375,687	103,449,685
Bus Rapid Transit	50,000,000	28,166,061	4,897,880
Grand Total	1,809,737,437	1,534,660,842	148,518,604



Construction undergoing at Barlow Trail and 114 Ave

Construction

- Work continues on the MSF site and Barlow Trail and 114 Avenue.
- Three more projects to begin in Q3: 78 Avenue LRT Bridge, Ogden Road Realignment, Blackfoot Trail LRT Bridge.

Procurement

- Three construction packages to be awarded in September.
- RFPQ for five civil works packages closing on September 22, 2025.

LRV Manufacturing

- Qualification testing of key systems planned for Q3 2025.

Downtown Functional Plan

- Finalize consultant contract and work plan.
- Continue team recruitment.

Recommendation:

That Executive Committee recommend Council receive this report for the Corporate Record.
